

Project Plan — The Witness

CLIENT

Nightfall Interactive

MADE BY

David Eslava, ICT Student

COACH

Frank & Faruk

PROJECT PERIOD

1 September – 25 September 2026 (4 weeks)

DEADLINE

Friday 25 September 2026, 16:00

1. What this plan is for

The Analysis says what I am building and why. This plan says when I do it, in what order, and how long each part takes. Frank asked for it as a separate document with a Gantt chart, activities, estimated hours and dependencies.

2. What gets delivered

Two things:

1. **A playable prototype** — a player moving through a walled map, an enemy patrolling a route, detection through a vision cone, and a game over when the player is caught.
2. **The documentation** — Analysis, Advice, Design, this plan, Validation, an orientation report and the devlog.

Anything marked Will Not Have in the Analysis is out of scope.

The adaptive Hunter is a Could Have and is not built in this delivery. My coach agreed to this on 22 September, because it sits in Could Have in the MoSCoW table. What I deliver instead is a complete design for The Hunter, including how its improvement would be measured, which is written up in the Design document. The stealth loop has to work before a learning enemy can be measured against it.

3. Phases

PHASE	WHEN	FINISHED WHEN
Analysis	Week 1–2	Analysis delivered to Frank
Advice	Week 3–4	Engine and AI choices written up with the reasoning
Design	Week 3–4	Architecture and flowcharts done
Realisation	Week 4	Prototype does everything in Must Have
Validation	Week 4	Tests run and written up
Delivery	25 September	Everything submitted before 16:00

4. Activities

Hours are estimates. Status is as of Wednesday 23 September.

ANALYSIS

ACTIVITY	HOURS	CAN'T START UNTIL	STATUS
Work out the concept, setting and core loop	4	—	Done
Compare game engines (Godot, Unity, GameMaker, Pygame)	6	concept is decided	Done
Research Q-learning for grid-based chasing	8	concept is decided	Done
Write the MoSCoW table	4	concept is decided	Done
Write the Analysis, first version	6	research and MoSCoW done	Done
Export it and send it to Frank	1	Analysis written	Done

ADVICE

ACTIVITY	HOURS	CAN'T START UNTIL	STATUS
Feedback meeting with Frank and write down what he said	2	Analysis sent	Done, 14 Sep
Write the Advice document — the engine and AI comparison, the trade-offs, why I chose what I chose	3	the research and the feedback	Wednesday

DESIGN

ACTIVITY	HOURS	CAN'T START UNTIL	STATUS
Draw the high-level flowchart	3	Analysis written	Done
Learn Godot through a tutorial project — nodes, scenes, tilemaps, collisions	12	engine chosen	Done
Build the player — eight-direction movement and the animation states	10	Godot basics	Done
Write the Design document — technical choices, how the scenes fit together, a detailed flowchart for detection only	4	Advice document	Wednesday

REALISATION

ACTIVITY	HOURS	CAN'T START UNTIL	STATUS
Build the map — tilemap, walls, collision	3	Design written	Wednesday
One enemy patrolling a fixed route	2	map exists	Wednesday
Vision cone and line-of-sight detection	3	enemy patrols	Wed–Thu
Game over and restart when caught	1.5	detection works	Thursday

VALIDATION


ACTIVITY	HOURS	CAN'T START UNTIL	STATUS
Write the test plan	1	prototype playable	Thursday
Playtest with two or three people	1.5	test plan	Thursday
Write the Validation document	1.5	tests run	Thursday

DOCUMENTATION AND PORTFOLIO

ACTIVITY	HOURS	CAN'T START UNTIL	STATUS
Write this plan	2	feedback meeting	Done
Rewrite the Analysis for the client	4	feedback meeting	Done
Finish the devlog and put it all in English	1	—	Thursday
Write the evidence descriptions for each piece	1.5	the piece exists	As I go
Write the orientation report	2	—	Friday
Final check and submit	1	everything else	Thursday

Total: 88 hours. 62 done, 26 left.

5. Gantt chart

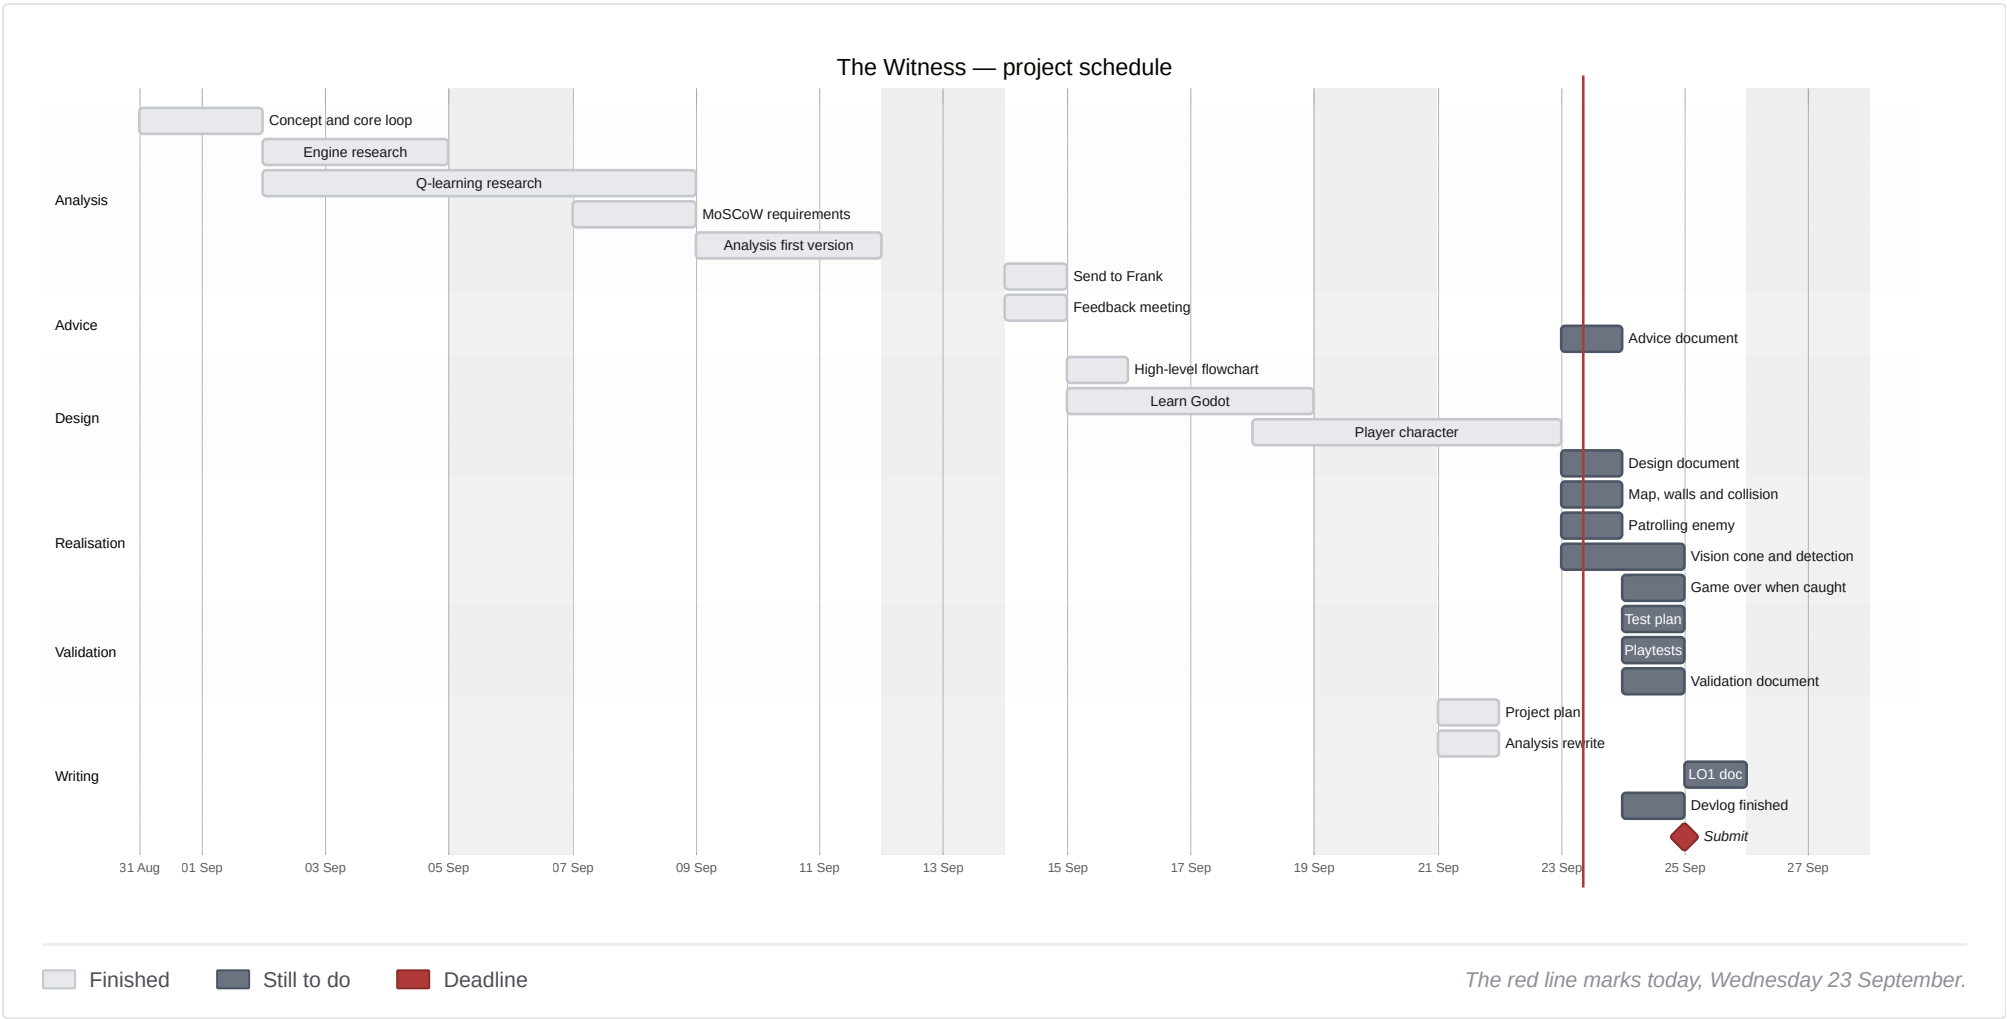

6. The rest of the week

DAY	WHAT I DO	HOURS
Mon 21	Project plan, Analysis rewrite	6, done
Tue 22	Analysis finished to version 0.2, portfolio reorganised by learning outcome	8, done
Wed 23	Advice document (1.5), Design document (2.5), map and walls (2.5), patrolling enemy (1.5)	8
Thu 24	Vision cone (2.5), game over (1), test plan and playtests (2), Validation (1.5), devlog into English (1), LO2 evidence descriptions (1)	9
Fri 25	Orientation doc (1.5), career choice and workshop log (1), core values and feedback log (1), remaining evidence descriptions (1), final check and submit (0.5)	5, finish by 13:00

I put the writing before the code on purpose. None of the documents need the game to compile, so if the prototype runs late the documentation is already safe. Friday was meant to be a buffer; losing Tuesday to the Analysis spent it.

7. What could go wrong

- **I am a day behind.** Tuesday went on finishing the Analysis and reorganising the portfolio instead of the Advice and Design documents. That means Friday morning is now working time, not buffer. I re-cut the schedule on Wednesday morning rather than discovering it on Thursday night.
- **Detection is the part most likely to eat the day.** I build the vision cone as a cone-shaped Area2D on the enemy that turns with it, plus one raycast so walls block sight. That is the simplest thing that still meets the Must Have. If it fights me for more than half a day I ship the Area2D on its own and say so in the Validation.
- **My sprites are 1024×1024 and the camera is zoomed to 0.3.** That makes a normal tileset awkward. So I build the map out of plain rectangles at the player's scale. Frank already said placeholders are fine.
- **Evidence descriptions get forgotten.** I write each one right after the thing it describes, not all of them on Thursday night.

If I fall behind, I cut in this order: the title and game over screens first, then the alert gauge, then the visual polish. The Must Haves and the documents don't get cut.

8. How I know I'm finished

- The prototype runs, and you can walk around a walled map, get spotted by a patrolling enemy, and get caught.
- All seven of Frank's points from 14 September are dealt with.
- Analysis, Advice, Design, this plan, Validation, the orientation report and the devlog are all there, finished, in English.
- Every piece has an evidence description saying why it's in the portfolio, what I learned, and what I'd do differently.
